




























ID	Task Name	Duration	Start	Finish	Pred	% Work Comp	March		
							26.1	23.2	23.3
1	Actual: Development project of AAI for Finnish language resour	291 days	Mon 23.3.09	Mon 3.5.10		0%			
2	Planning	74 days	Mon 23.3.09	Thu 2.7.09		100%			
3	Requirements Specification review	28 days	Mon 23.3.09	Wed 29.4.09		100%			
4	Project plan	18 days	Thu 30.4.09	Mon 25.5.09	3	100%			
5	<i>Requirements Documentation (additional work)</i>	28 days	Tue 26.5.09	Thu 2.7.09	4	100%			
6	Shibboleth authentication	10 days	Fri 3.7.09	Thu 16.7.09	5	10%			
7	Controlled authorization	70 days	Fri 17.7.09	Thu 22.10.09		0%			
8	Architecture design	10 days	Fri 17.7.09	Thu 30.7.09	6	80%			
9	Required attributes	5 days	Fri 31.7.09	Thu 6.8.09	8	10%			
10	Application form	10 days	Fri 7.8.09	Thu 20.8.09	9	80%			
11	MySQL language bank database	5 days	Fri 21.8.09	Thu 27.8.09	10	70%			
12	Other database changes	15 days	Fri 28.8.09	Thu 17.9.09	11	50%			
13	Referee's authorization	10 days	Fri 18.9.09	Thu 1.10.09	12	0%			
14	Content provider's acceptance	5 days	Fri 2.10.09	Thu 8.10.09	13	0%			
15	Administrator's acceptance	5 days	Fri 9.10.09	Thu 15.10.09	14	0%			
16	Resource list (Language Bank)	5 days	Fri 16.10.09	Thu 22.10.09	15	80%			
17	Authentication (non-Shibboleth)	10 days	Fri 23.10.09	Thu 5.11.09		0%			
18	Email confirmation	5 days	Fri 23.10.09	Thu 29.10.09	16	0%			
19	Referee authentication	5 days	Fri 30.10.09	Thu 5.11.09	18	0%			
20	Automatic authorization	42 days	Fri 6.11.09	Mon 4.1.10		0%			
21	Architecture design	10 days	Fri 6.11.09	Thu 19.11.09	19	0%			
22	Required attributes	5 days	Fri 20.11.09	Thu 26.11.09	21	0%			
23	MySQL language bank database	5 days	Fri 27.11.09	Thu 3.12.09	22	0%			
24	Resource manager	17 days	Fri 4.12.09	Mon 28.12.09	23	0%			
25	Resource list (Language Bank)	5 days	Tue 29.12.09	Mon 4.1.10	24	0%			
26	Testing	85 days	Tue 5.1.10	Mon 3.5.10		0%			
27	1st alpha version available for CSC internal testing	25 days	Tue 5.1.10	Mon 8.2.10	25	0%			
28	1st beta version available for UHEL representatives	25 days	Tue 9.2.10	Mon 15.3.10	27	0%			
29	1st release candidate for pilot users	25 days	Tue 16.3.10	Mon 19.4.10	28	0%			
30	Opening service for customers	10 days	Tue 20.4.10	Mon 3.5.10		0%			
31	Generate Statistics	5 days	Tue 20.4.10	Mon 26.4.10	29	0%			


Project: Kalle schedule Date: Fri 25.9.09	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

ID	Task Name	Duration	Start	Finish	Pred	% Work Comp	March		
							26.1	23.2	23.3
32	Inform users	5 days	Tue 27.4.10	Mon 3.5.10	31	0%			
33									
34									
35									

Project: Kalle schedule Date: Fri 25.9.09	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

ID	Task Name	Duration	Start	Finish	Pred	% Work Comp	March		
							26.1	23.2	23.3
36	Original plan: Development project of AAI for Finnish language	258 days	Mon 23.3.09	Wed 17.3.10		0%			
37	Planning	41 days	Mon 23.3.09	Mon 18.5.09		0%			
38	Requirements Specification review	28 days	Mon 23.3.09	Wed 29.4.09		0%			
39	Project plan	13 days	Thu 30.4.09	Mon 18.5.09	38	0%			
40	Shibboleth authentication	10 days	Tue 19.5.09	Mon 1.6.09	39	0%			
41	Controlled authorization	70 days	Tue 2.6.09	Mon 7.9.09		0%			
42	Architecture design	10 days	Tue 2.6.09	Mon 15.6.09	40	0%			
43	Required attributes	5 days	Tue 16.6.09	Mon 22.6.09	42	0%			
44	Application form	10 days	Tue 23.6.09	Mon 6.7.09	43	0%			
45	MySQL language bank database	5 days	Tue 7.7.09	Mon 13.7.09	44	0%			
46	Other database changes	15 days	Tue 14.7.09	Mon 3.8.09	45	0%			
47	Referee's authorization	10 days	Tue 4.8.09	Mon 17.8.09	46	0%			
48	Content provider's acceptance	5 days	Tue 18.8.09	Mon 24.8.09	47	0%			
49	Administrator's acceptance	5 days	Tue 25.8.09	Mon 31.8.09	48	0%			
50	Resource list (Language Bank)	5 days	Tue 1.9.09	Mon 7.9.09	49	0%			
51	Authentication (non-Shibboleth)	10 days	Tue 8.9.09	Mon 21.9.09		0%			
52	Email confirmation	5 days	Tue 8.9.09	Mon 14.9.09	50	0%			
53	Referee authentication	5 days	Tue 15.9.09	Mon 21.9.09	52	0%			
54	Automatic authorization	42 days	Tue 22.9.09	Wed 18.11.09		0%			
55	Architecture design	10 days	Tue 22.9.09	Mon 5.10.09	53	0%			
56	Required attributes	5 days	Tue 6.10.09	Mon 12.10.09	55	0%			
57	MySQL language bank database	5 days	Tue 13.10.09	Mon 19.10.09	56	0%			
58	Resource manager	17 days	Tue 20.10.09	Wed 11.11.09	57	0%			
59	Resource list (Language Bank)	5 days	Thu 12.11.09	Wed 18.11.09	58	0%			
60	Testing	85 days	Thu 19.11.09	Wed 17.3.10		0%			
61	1st alpha version available for CSC internal testing	25 days	Thu 19.11.09	Wed 23.12.09	59	0%			
62	1st beta version available for UHEL representatives	25 days	Thu 24.12.09	Wed 27.1.10	61	0%			
63	1st release candidate for pilot users	25 days	Thu 28.1.10	Wed 3.3.10	62	0%			
64	Opening service for customers	10 days	Thu 4.3.10	Wed 17.3.10		0%			
65	Generate Statistics	5 days	Thu 4.3.10	Wed 10.3.10	63	0%			
66	Inform users	5 days	Thu 11.3.10	Wed 17.3.10	65	0%			

Project: Kalle schedule Date: Fri 25.9.09	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

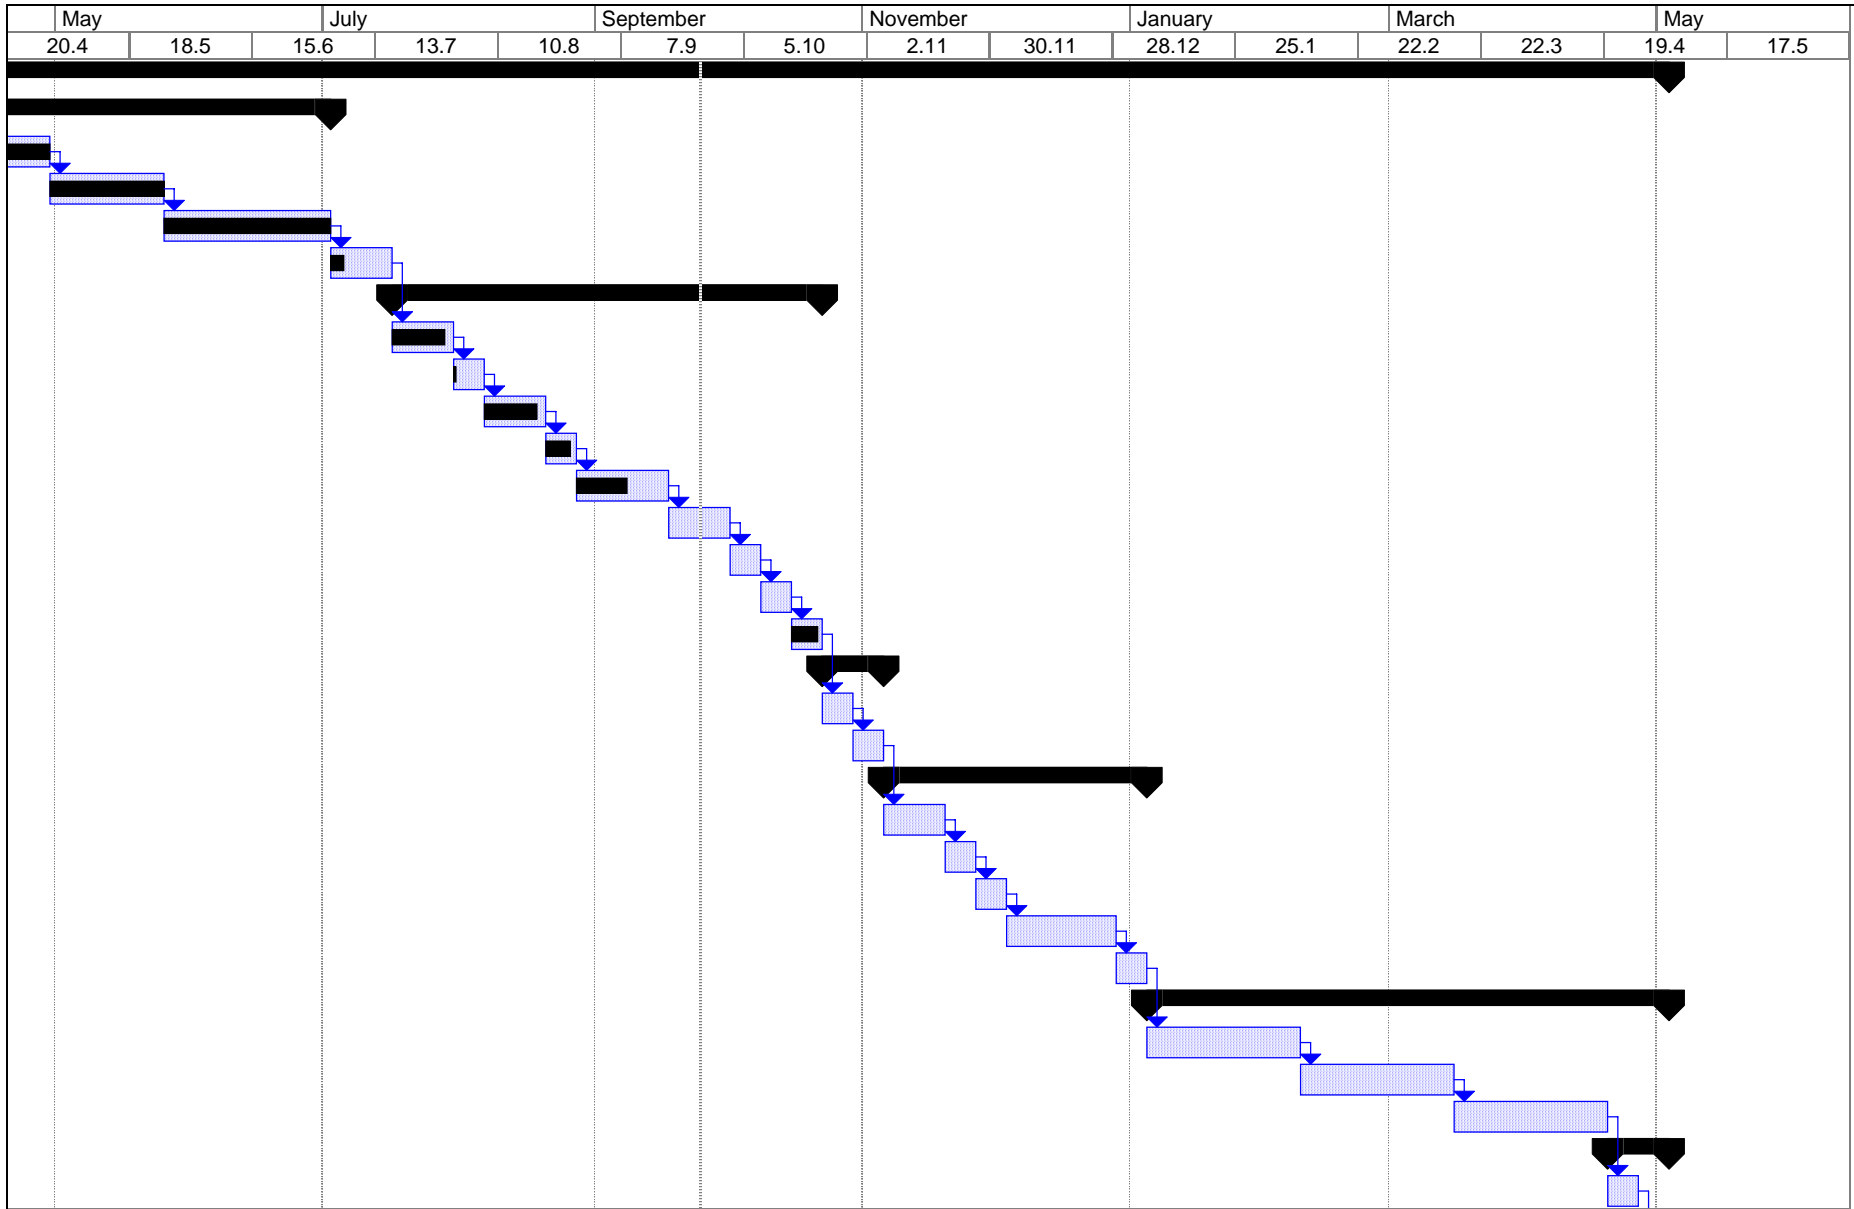








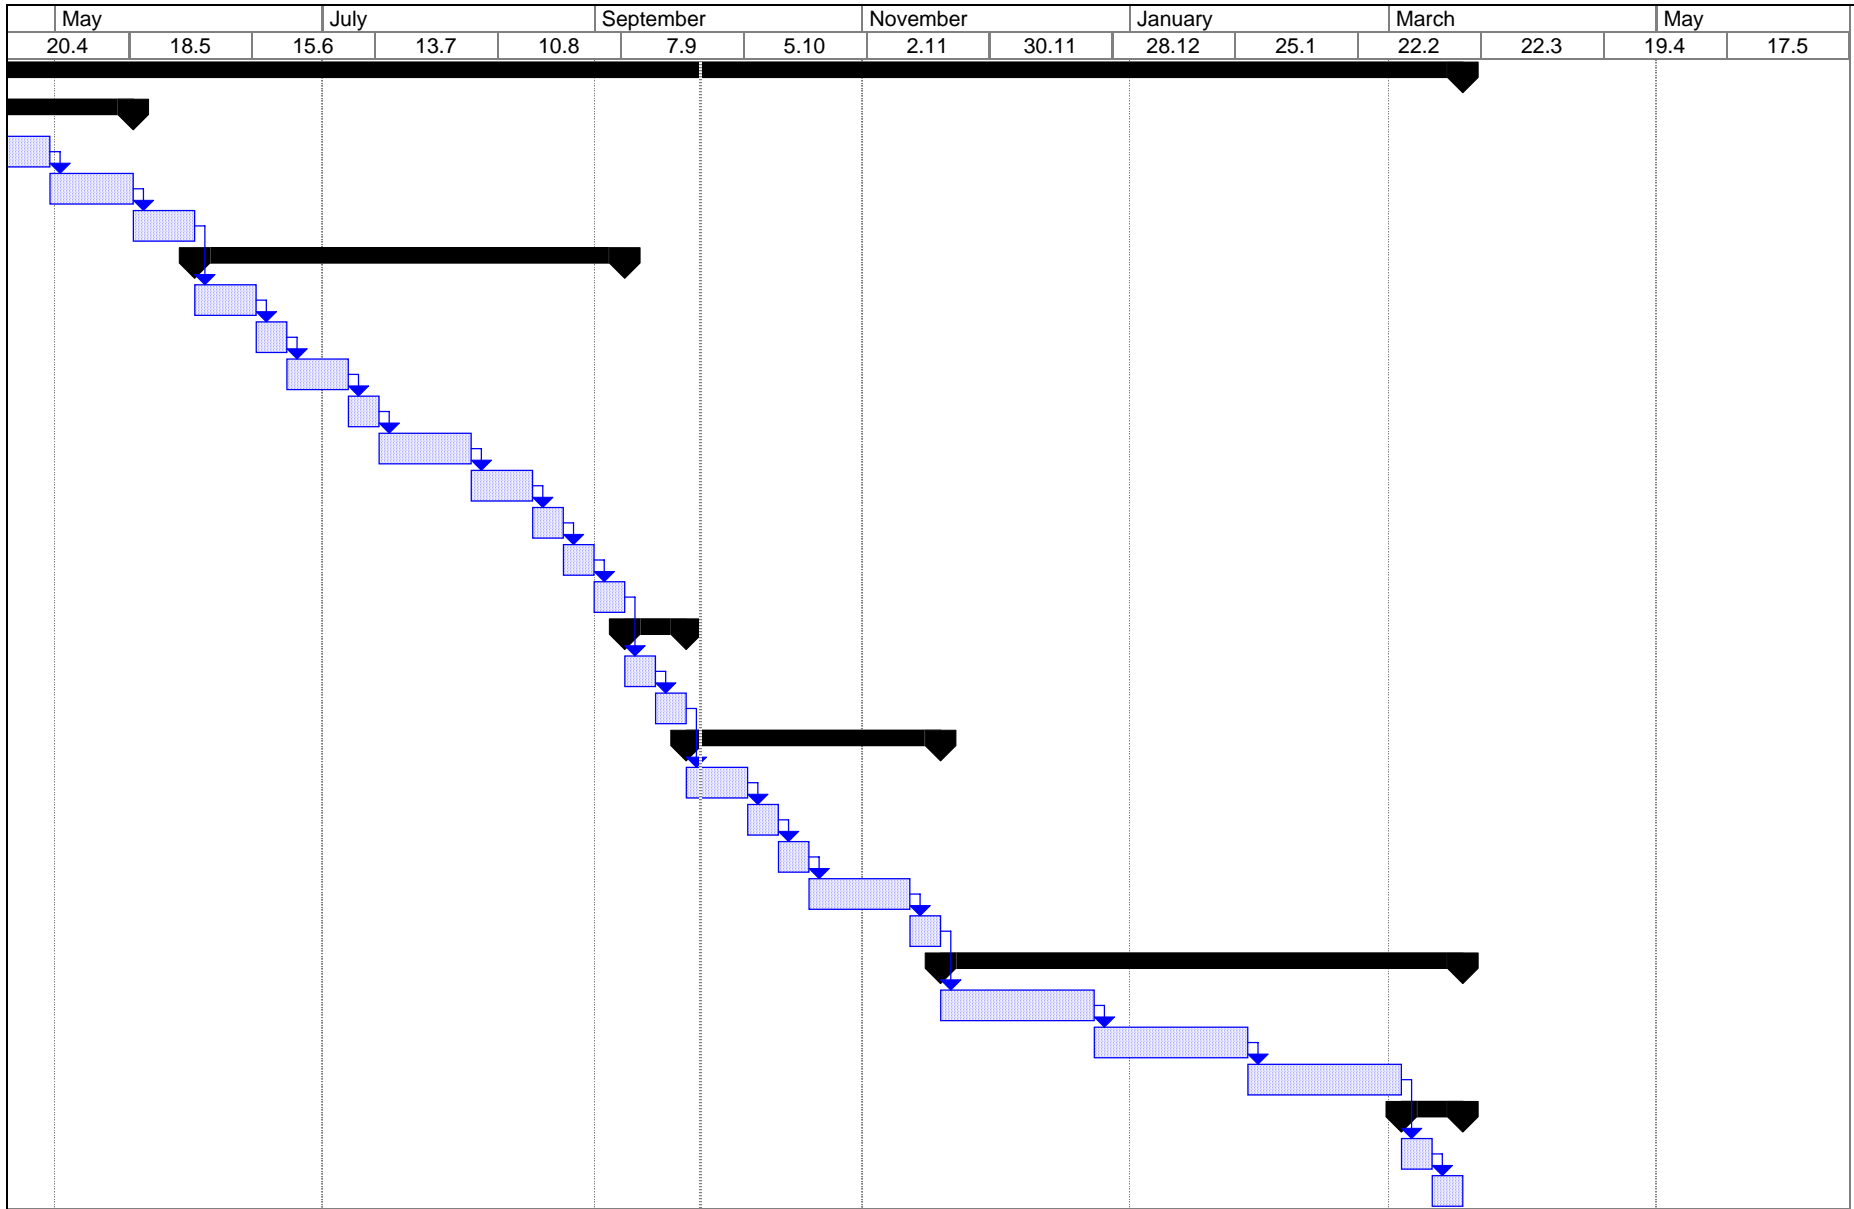

Project: Kalle schedule Date: Fri 25.9.09	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

May		July			September		November		January		March		May	
20.4	18.5	15.6	13.7	10.8	7.9	5.10	2.11	30.11	28.12	25.1	22.2	22.3	19.4	17.5

Project: Kalle schedule
Date: Fri 25.9.09

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	



Project: Kalle schedule Date: Fri 25.9.09	Task 	Milestone 	External Tasks 
	Split 	Summary 	External Milestone 
	Progress 	Project Summary 	Deadline 
